

CONTRACT NO. OSM PA (813) 101.5

PROJECT NO. OSM 40(5123)101.5

PITTSTON, PA.

SITE 3

HOLE No. 15 DEPTH DRILLED (COMPLETED) 125.0 LFT.  
DEPTH DRILLED (BEGINNING) 0 LFT.

HOLE No. 16 DEPTH DRILLED (COMPLETED) 118.0 LFT.  
DEPTH DRILLED (BEGINNING) 0 LFT.


DATE DRILLED: 30 APRIL 1986

DATE DRILLED: 28 MAY 1986

SURFACE ELEVATION:

SURFACE ELEVATION:


DRILLING RUNS (ft.)		% CORE RECOV.
FROM	TO	
0	38	
38	45	100
45	54	77
54	58	95
58	64	73
64	68.5	64
68.5	75	100
75	85	100
85	95	100
95	105	100
105	115	16
115	125	76

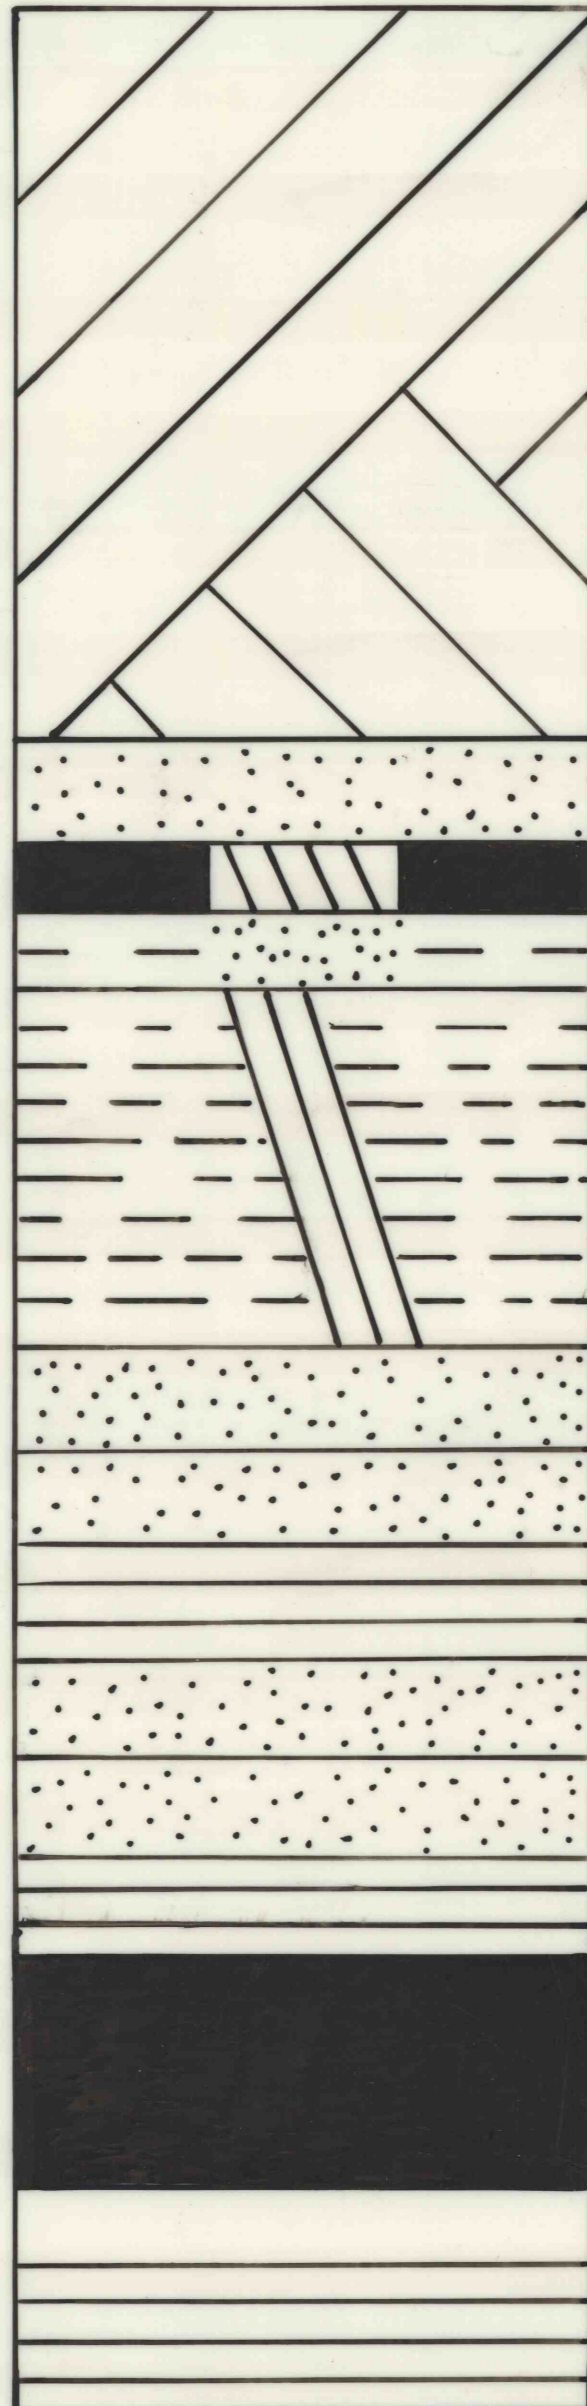

FIELD CLASSIFICATION OF MATERIALS
OVERBURDEN
GR. MED. HARD SANDSTONE COAL + GRAY CLAY
GR. BR. SHALE W/SANDSTONE STRS.
GRAY BADLY BROKEN SHALE + CLAY
GRAY MED. HARD SANDSTONE W/SHALE STRS.
GRAY SHALE
COAL
VOID
DK GRAY SHALE

TOP OF ROCK 38.0  
LOST WATER 95.0  
BOTTOM OF HOLE 125.0  
CEMENT HOLE 48.0 - 38.0

DRILLING RUNS (ft.)		% CORE RECOV.
FROM	TO	
0	40	
40	44	85
44	54	60
54	64	47
64	74	46
74	84	100
84	94	80
94	104	100
104	114	40
114	118	100

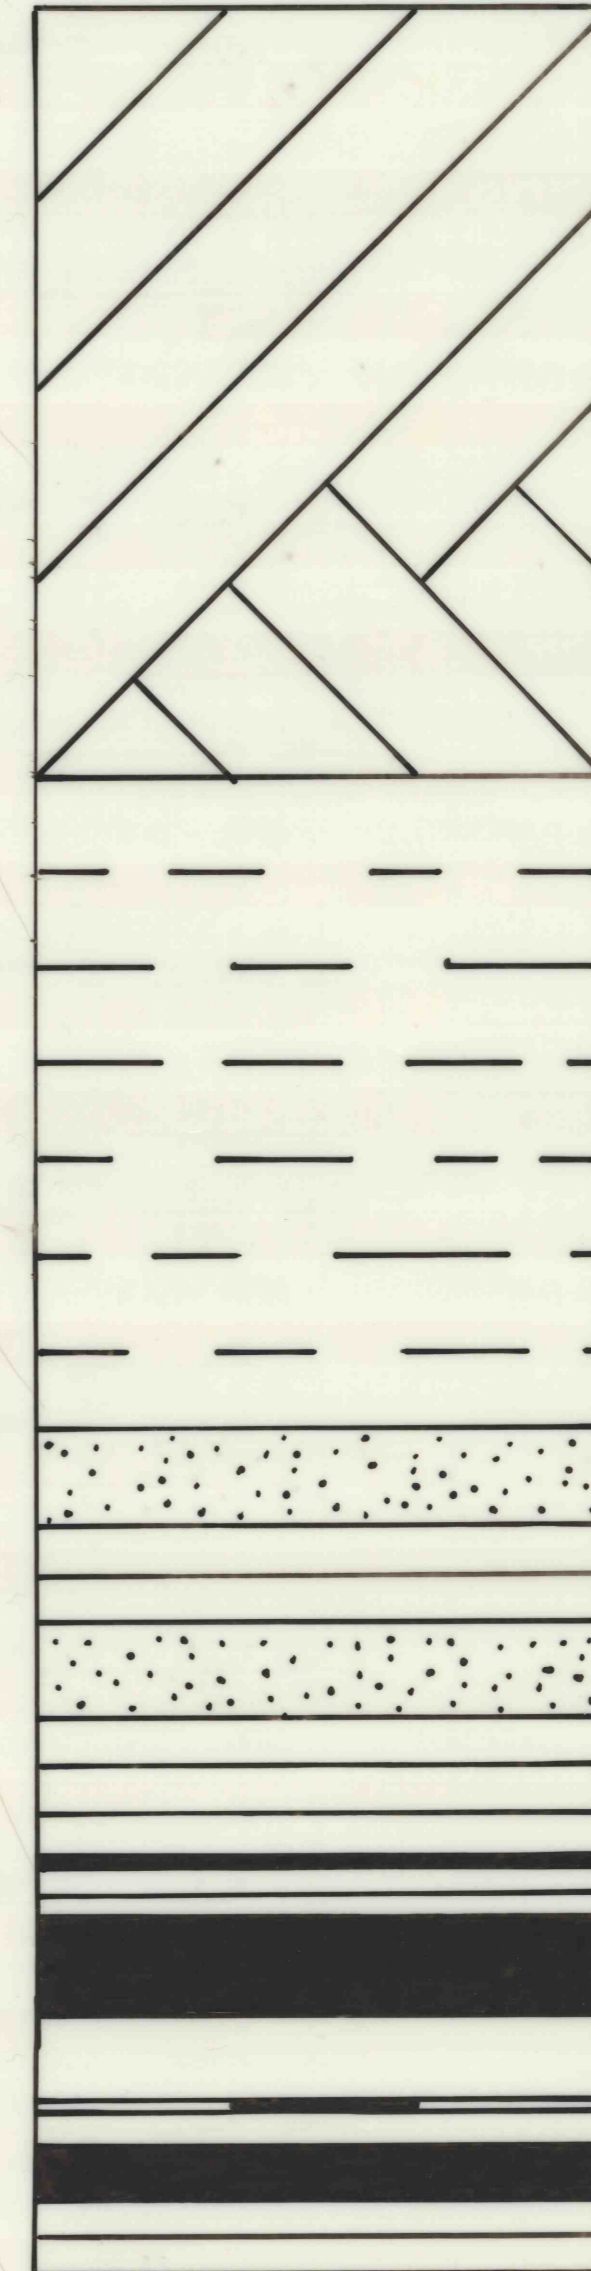

FIELD CLASSIFICATION OF MATERIALS
OVERBURDEN
GRAY BADLY BROKEN SANDSTONE
GR. MED. HARD SANDSTONE W/SHALE STREAKS
DK. GRAY SHALE
DK. GRAY SHALE
COAL
VOID (4.2)
VOID (1.8)
COAL
GRAY SHALE

TOP OF ROCK 40.0  
BOTTOM OF HOLE 118.0  
LOST WATER 81.2  
WATER LEVEL 86.0  
CEMENT HOLE 50.0 - 40.0
